

**BOARD OF PUBLIC WORKS AND SAFETY  
Agenda Request Form**

(Form B-01-2012)

*Organizations and individuals are asked to submit a request form and supporting documents to be placed on the agenda. You will be contacted by the City confirming the date of the meeting in which your request will be heard. Please make sure that your contact information is accurate in case we need to get in touch with you. The Board of Works meets on the 1st and 3rd Monday of each month at 5:00 p.m. in City Hall located at 70 E. Monroe Street.*

<b>Date Submitted:</b>	03/30/2022	<b>Meeting Date:</b>	04/18/2022
<b>Contact Information:</b>			
<b>Requested by:</b>	Sally Brown		
<b>On Behalf of Organization or Individual</b>	Wessler Engineering		
<b>Telephone:</b>	317-736-3640		
<b>Email address:</b>	sbrown@franklin.in.gov		
<b>Mailing Address:</b>	796 South State Street, Franklin, IN 46131		
<b>Describe Request</b>			
Change Order No. 3 for Eastside Regional Interceptor & Lift Station			
<b>List Supporting Documentation Provided:</b>			
Change Order No. 3			
<b>Who will present the request?</b>			
<b>Name:</b>	Gary Ruston, Wessler Engineering	<b>Telephone:</b>	317-788-4551

*In order for an individual and/or agency to be considered for new business on the Board of Works agenda, this reservation form and supporting documents must be received in the Mayor's office no later than 4:00 p.m. on the Wednesday before the meeting.*

Change Order No. 3

Date of Issuance: April 18, 2022	Effective Date: March 21, 2022
Owner: City of Franklin, Indiana	Owner's Contract No.:
Contractor: Atlas Excavating, Inc.	Contractor's Project No.:
Engineer: Wessler Engineering	Engineer's Project No.: 220819
Project: East Side Regional Interceptor and Lift Station	Contract Name:

The Contract is modified as follows upon execution of this Change Order:

Description: See Attachment A

Attachments: See Attachment A

CHANGE IN CONTRACT PRICE	CHANGE IN CONTRACT TIMES [note changes in Milestones if applicable]
Original Contract Price:  \$ <u>3,629,925.00</u>	Original Contract Times: Substantial Completion: <u>300 calendar days (March 19, 2022)</u> Ready for Final Payment: <u>345 calendar days (May 3, 2022)</u> days or dates
Increase from previously approved Change Order Nos. 1 & 2:  \$ <u>102,501.80</u>	Increase from previously approved Change Order Nos. 1 & 2: Substantial Completion: <u>30 days</u> Ready for Final Payment: <u>30 days</u> days
Contract Price prior to this Change Order:  \$ <u>3,732,426.80</u>	Contract Times prior to this Change Order: Substantial Completion: <u>330 calendar days (April 18, 2022)</u> Ready for Final Payment: <u>375 calendar days (June 3, 2022)</u> days or dates
[Increase] [Decrease] of this Change Order:  \$ <u>N/A</u>	Increase of this Change Order: Substantial Completion: <u>35 calendar days</u> Ready for Final Payment: <u>0 calendar days</u> days or dates
Contract Price incorporating this Change Order:  \$ <u>3,732,426.80</u>	Contract Times with all approved Change Orders: Substantial Completion: <u>365 calendar days (May 23, 2022)</u> Ready for Final Payment: <u>375 calendar days (June 3, 2022)</u> days or dates

<b>RECOMMENDED:</b>		<b>ACCEPTED:</b>		<b>ACCEPTED:</b>	
By: <u>Monte A. Gardner</u>	<small>Digitally signed by Monte A. Gardner DN: cn=EJCDC, email=montegardner@wessler.com, c=Indiana, ou=Engineers Joint Contract Documents Committee, o=Engineers Joint Contract Documents Committee</small>	By: _____	Owner (Authorized Signature)	By: <u>[Signature]</u>	Contractor (Authorized Signature)
Title: <u>Sr. Constr. Project Mgr</u>		Title: _____		Title: <u>Project Manager</u>	
Date: <u>3/30/2022</u>		Date: _____		Date: <u>3.29.2022</u>	

Approved by Funding Agency (if applicable)

By: \_\_\_\_\_ Date: \_\_\_\_\_  
Title: \_\_\_\_\_

## ATTACHMENT A

### DESCRIPTION, PURPOSE & JUSTIFICATION CHANGE ORDER NO. 3

WESSLER PROJECT 220819

PROJECT: East Side Regional Interceptor and Lift Station

OWNER: City of Franklin, IN

CONTRACTOR: Atlas Excavating, Inc.

<u>DESCRIPTION, PURPOSE &amp; JUSTIFICATION OF CHANGE</u>	<u>ADD</u>	<u>DEDUCT</u>
<u>Item No. 1 – Request for Additional Time</u>	-0-	-0-
<u>Attached Correspondence:</u> Atlas RFI No. 33 – Request for Additional Time dated March 21, 2022		
Due to abnormal weather amounts the project area has encountered leading to less than suitable site conditions, Contractor has requested a 35-day time extension for Substantial Completion. Final Completion is not impacted.		
Total Additions and Deletions	-0-	-0-
<b>TOTAL ADD OF CHANGE ORDER NO. 3</b>		<b>-0-</b>

The net change in the contract amount for items identified in the Change order is zero.

The change in the Substantial Completion date has been approved resulting in 35 days being added to the Substantial Completion time. No extension has been granted for Final Completion.



**Atlas Excavating**  
4740 Swisher Road  
West Lafayette, Indiana 47906  
P: (765)-429-4800  
F: 7654298034

**Project: F21-07 Franklin Eastside Regional Interceptor  
& Lift Station**  
Franklin, Indiana

## RFI #33: Time Extension

<b>Status</b>	Open		
<b>To</b>	Jonathan Leinberger (Atlas Excavating)	<b>From</b>	Jonathan Leinberger (Atlas Excavating) 4740 Swisher Rd West Lafayette, Indiana 47906
<b>Date Initiated</b>	Mar 21, 2022	<b>Due Date</b>	Mar 24, 2022
<b>Location</b>	<b>Project Stage</b>		
<b>Cost Impact</b>	<b>Schedule Impact</b>		
<b>Spec Section</b>	<b>Cost Code</b>		
<b>Drawing Number</b>	<b>Reference</b>		
<b>Linked Drawings</b>			
<b>Received From</b>	Jonathan Leinberger (Atlas Excavating)		
<b>Copies To</b>	Tom Drollinger (Atlas Excavating), Scott Medley (Atlas Excavating)		

### Activity

#### Question

**Question from Jonathan Leinberger Atlas Excavating on Monday, Mar 21, 2022 at 01:05 PM EDT**  
Please see the attached Time Extension Request.

**Attachments**  
[Franklin time Extension 3.21.2022.pdf](#)

*Awaiting an Official Response*



March 21, 2022

Gary Ruston  
Monte Gardner  
Wessler Engineering  
6219 South East Street  
Indianapolis, Indiana 46227

Reference: Franklin Eastside Interceptor

Subject: Request for Additional Time

To Whom It May Concern:

The purpose of this letter is to request additional time on the above referenced contract. Pursuant to 4.05 C 3 in the contract documents, Atlas is requesting a time extension due to **abnormal weather and site conditions**. Due to the amount of rain and snow (10.26") the project area encountered since 1.22.2022, this led to less than suitable site conditions. This has also led to a loss in production that we are having troubles getting back in front of. The amount of site water that we have encountered has led to slower production times, added dewatering, added work to install pipe, and tougher conditions to maneuver in.

We believe by pushing increasing Substantial Completion 1 month, pushing this date to 5.23.2022, this will allow us substantial time to complete the pipe, LS demo, and any restoration that goes with it.

Please let me know if you have any questions.

Respectfully,

Jonathan Leinberger  
Project Manager  
Atlas Excavating, Inc.

Jonathan Leinberger  
Digitally signed by Jonathan  
Leinberger  
DN: cn=US,  
e=jleinberger@atlasexcavating.com,  
ou=Atlas Excavating, ou=Project  
Manager, cn=Jonathan Leinberger  
Date: 2022.03.21 13:00:57 -0400

4740 SWISHER ROAD, WEST LAFAYETTE, IN 47906

PHONE: (765) 429-4800 FAX: (765) 429-8034


Equal Opportunity Employer

Daily Weekly Monthly

View

2022

February

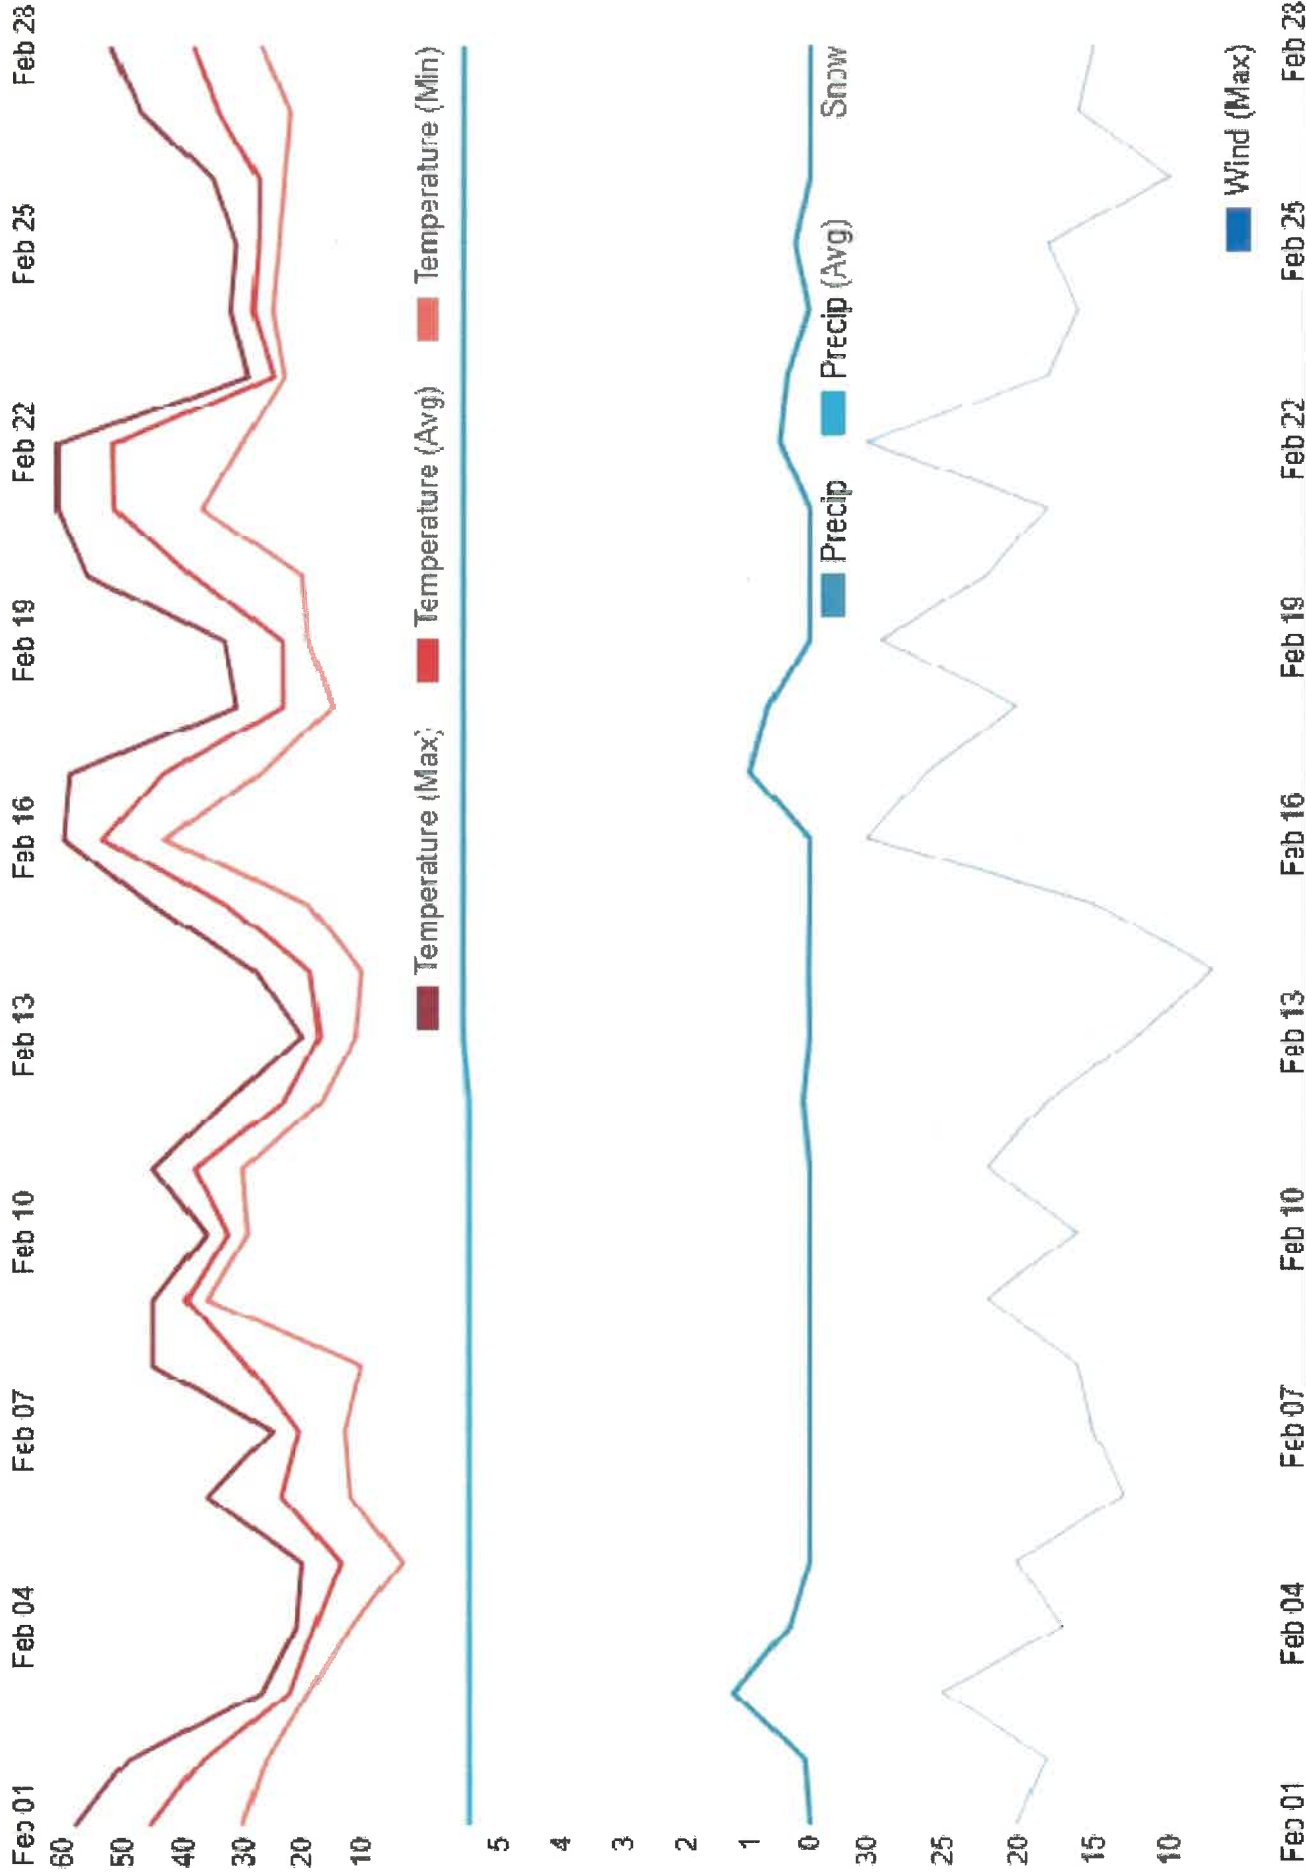

# Summary


Temperature (° F)	Max	Average	Min	▲
Max Temperature	61	40	20	
Avg Temperature	53.38	31.29	13.52	
Min Temperature	43	21.86	3	
Dew Point (° F)	Max	Average	Min	▲
Dew Point	57	22.28	-1	
Precipitation (Inches)	Max	Average	Min	Sum ▲
Precipitation	1.24	0.16	0.00	4.57
Snowdepth	3.00	0.11	0.00	3.00
Wind	Max	Average	Min	▲
Wind	30	11.02	0	
Gust Wind	46	4.14	0	
Sea Level Pressure	Max	Average	Min	▲
Sea Level Pressure	29.68	29.29	28.75	

Daily Weekly Monthly

March

2022

View

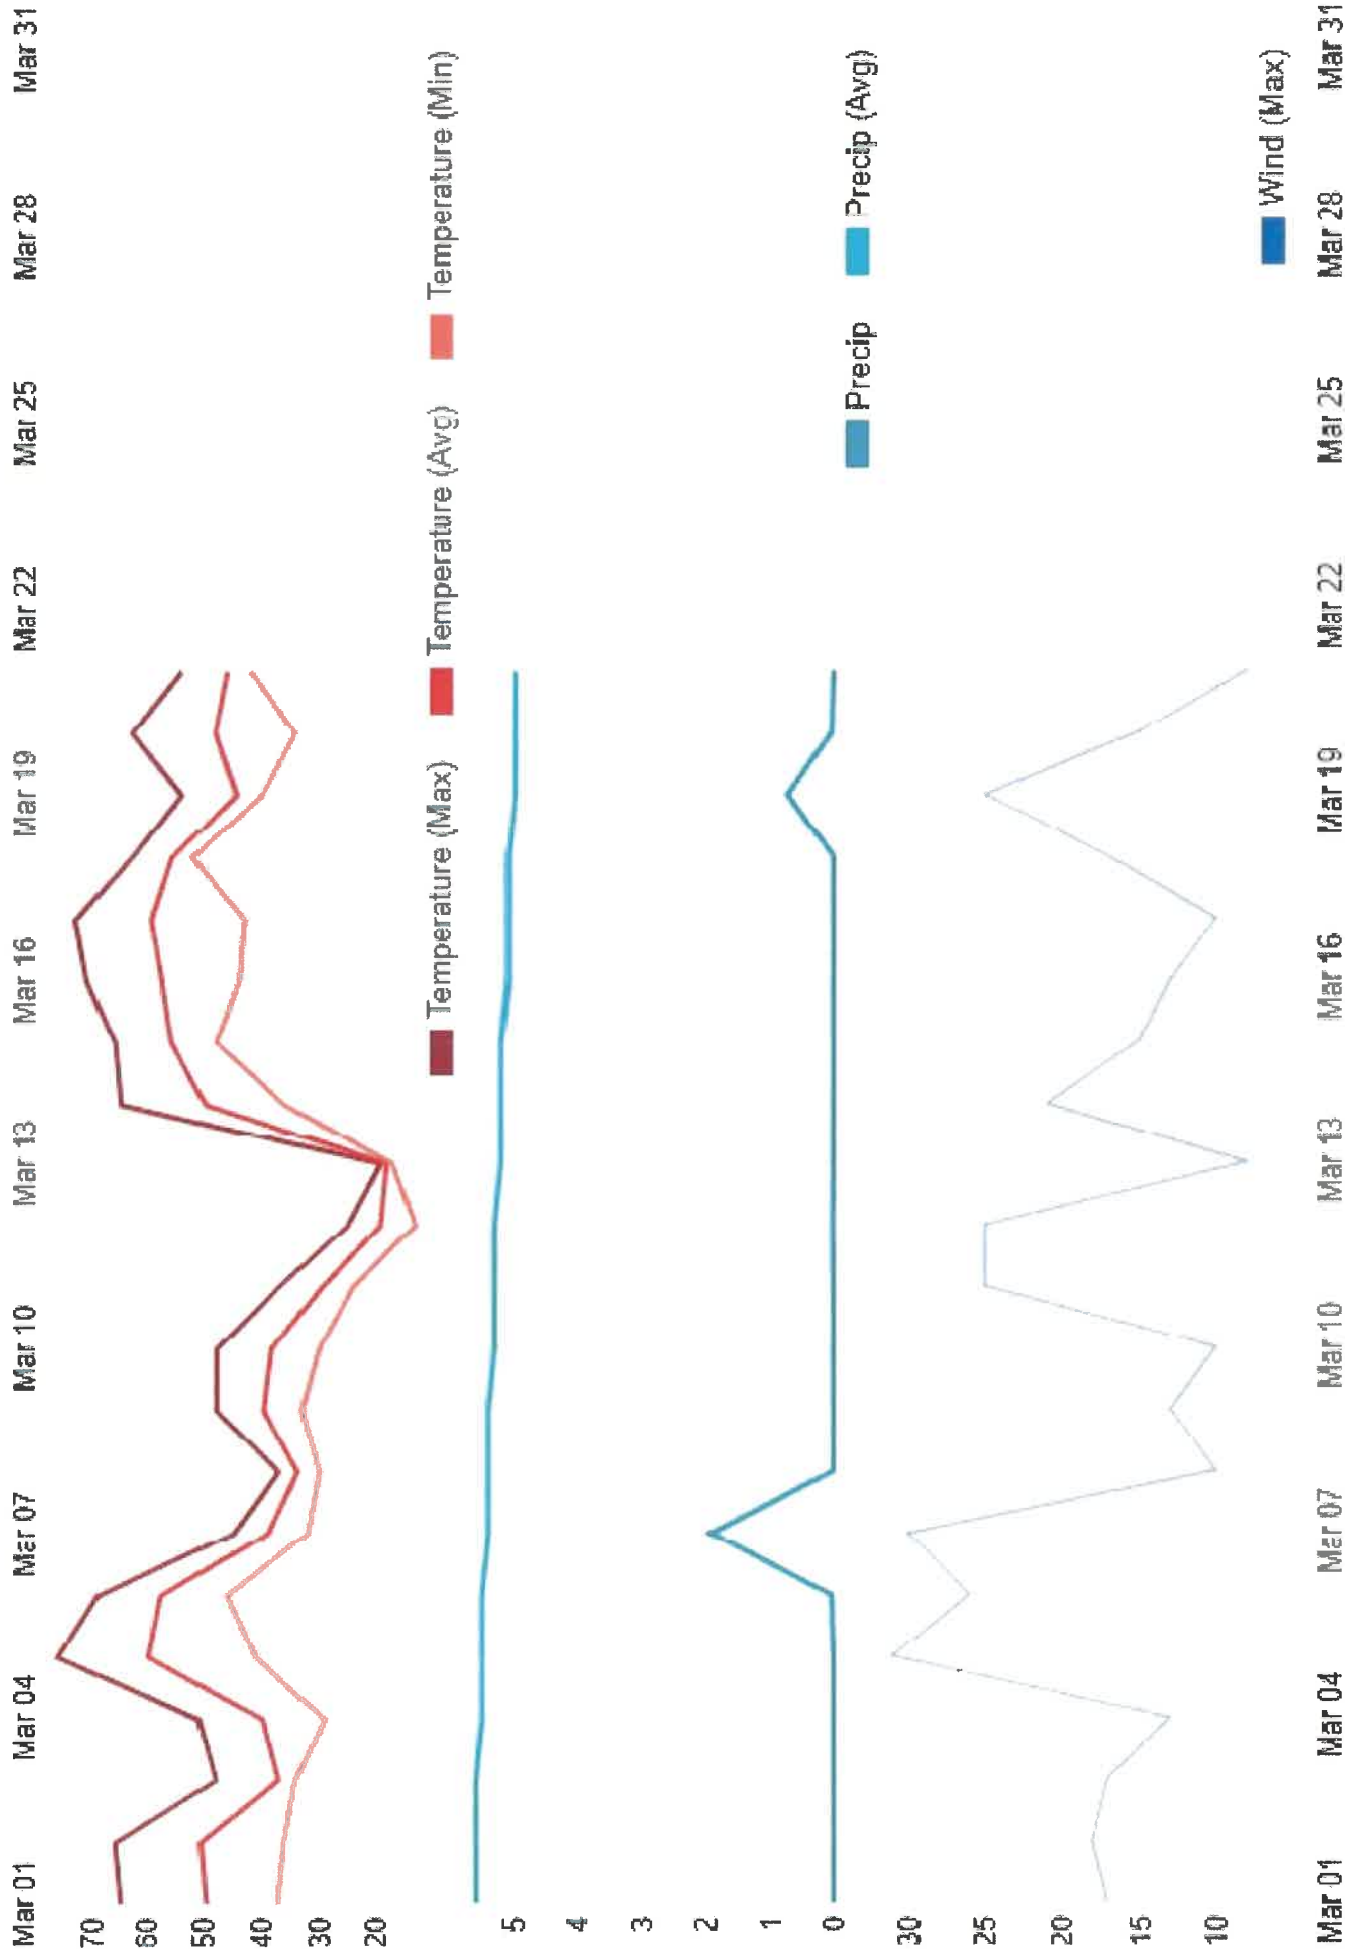



# Summary

Temperature (° F)	Max	Average	Min	
Max Temperature	76	54.43	19	
Avg Temperature	60	44.27	18	
Min Temperature	52	35.29	13	
Dew Point (° F)	Max	Average	Min	
Dew Point	57	30.49	1	
Precipitation (inches)	Max	Average	Min	Sum
Precipitation	1.51	0.13	0.00	2.69
Snowdepth	0.00	0.00	0.00	0.00
Wind	Max	Average	Min	
Wind	31	10.06	0	
Gust Wind	45	4.33	0	
Sea Level Pressure	Max	Average	Min	
Sea Level Pressure	29.54	29.21	28.75	
